

正覺寺玄奘文化宗教園區開發案

202307/21第一次變更設計完成

進度管理

	工程進度	目標工期	實際完成
1-1	開工前行政程序		
1-1-1	申報開工	2022/07/15	2022/07/19
1-1-2	放樣勘驗	2022/07/26	2022/07/28
1-1-3	第一次變更設計	2023/07/21	2023/07/21


正覺寺玄奘文化宗教園區開發案

範疇管理




工地全景(1120907)


● 目標進度管控表 (汙水處理廠)

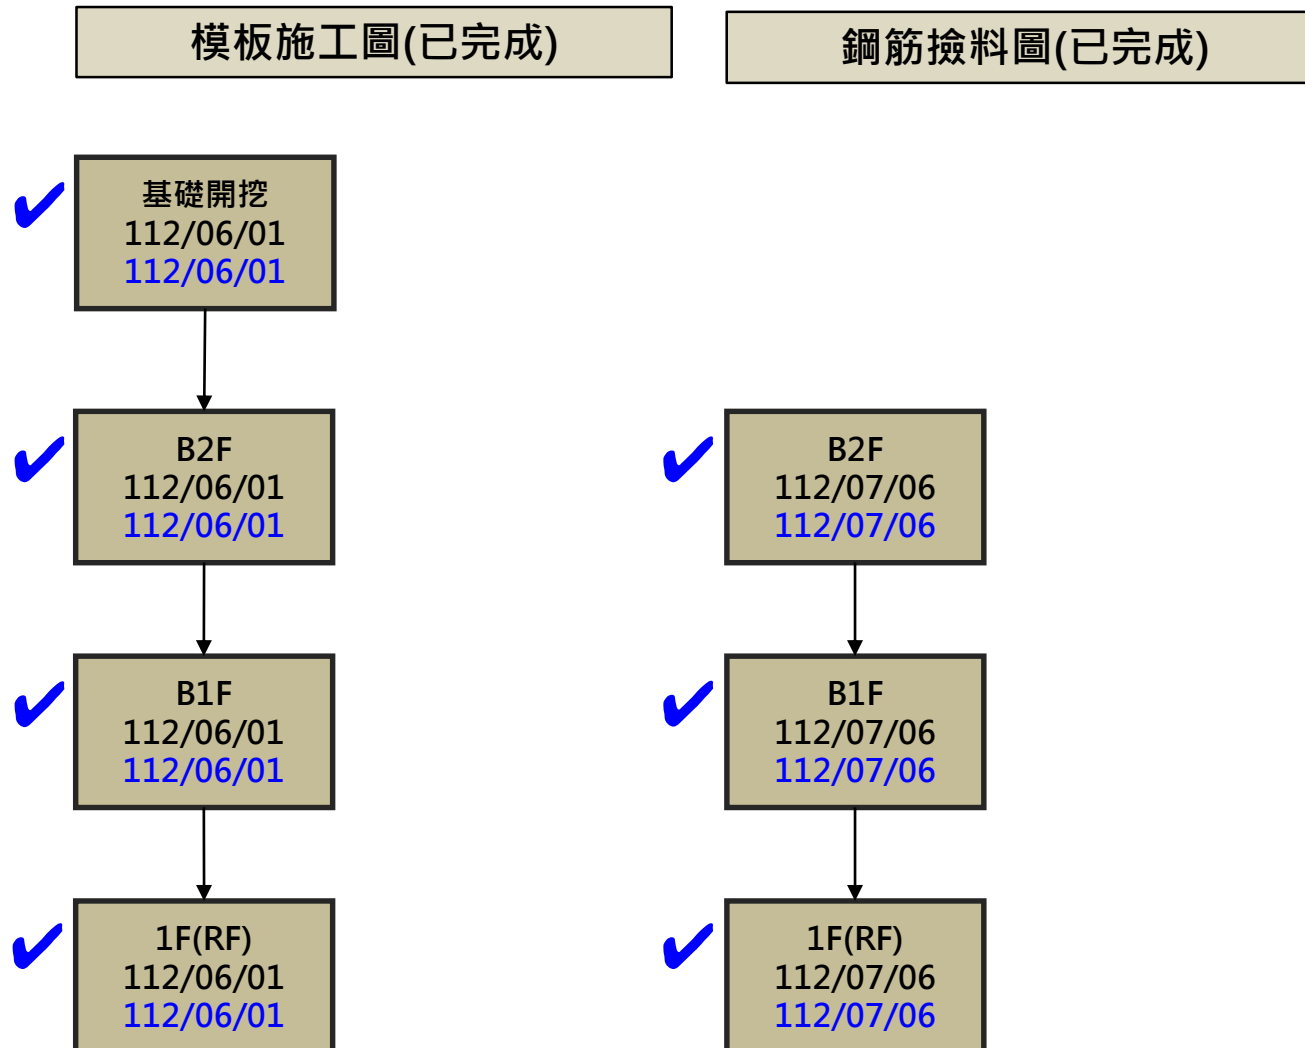


● 目標進度管控表 (D女寮)

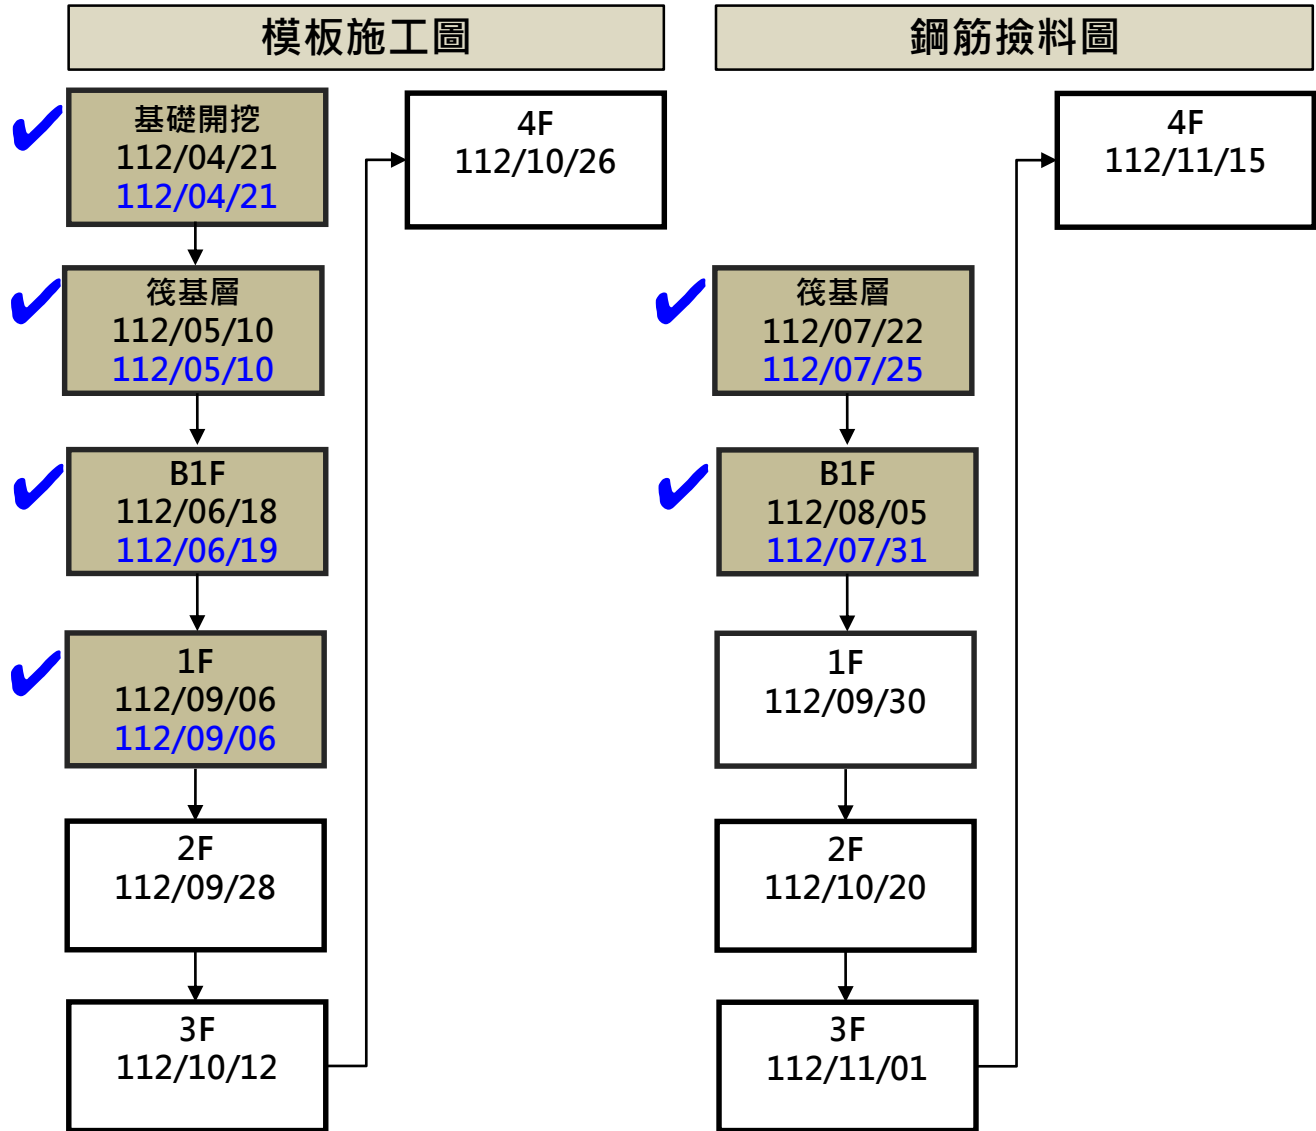


● 目標進度管控表 (A主殿)

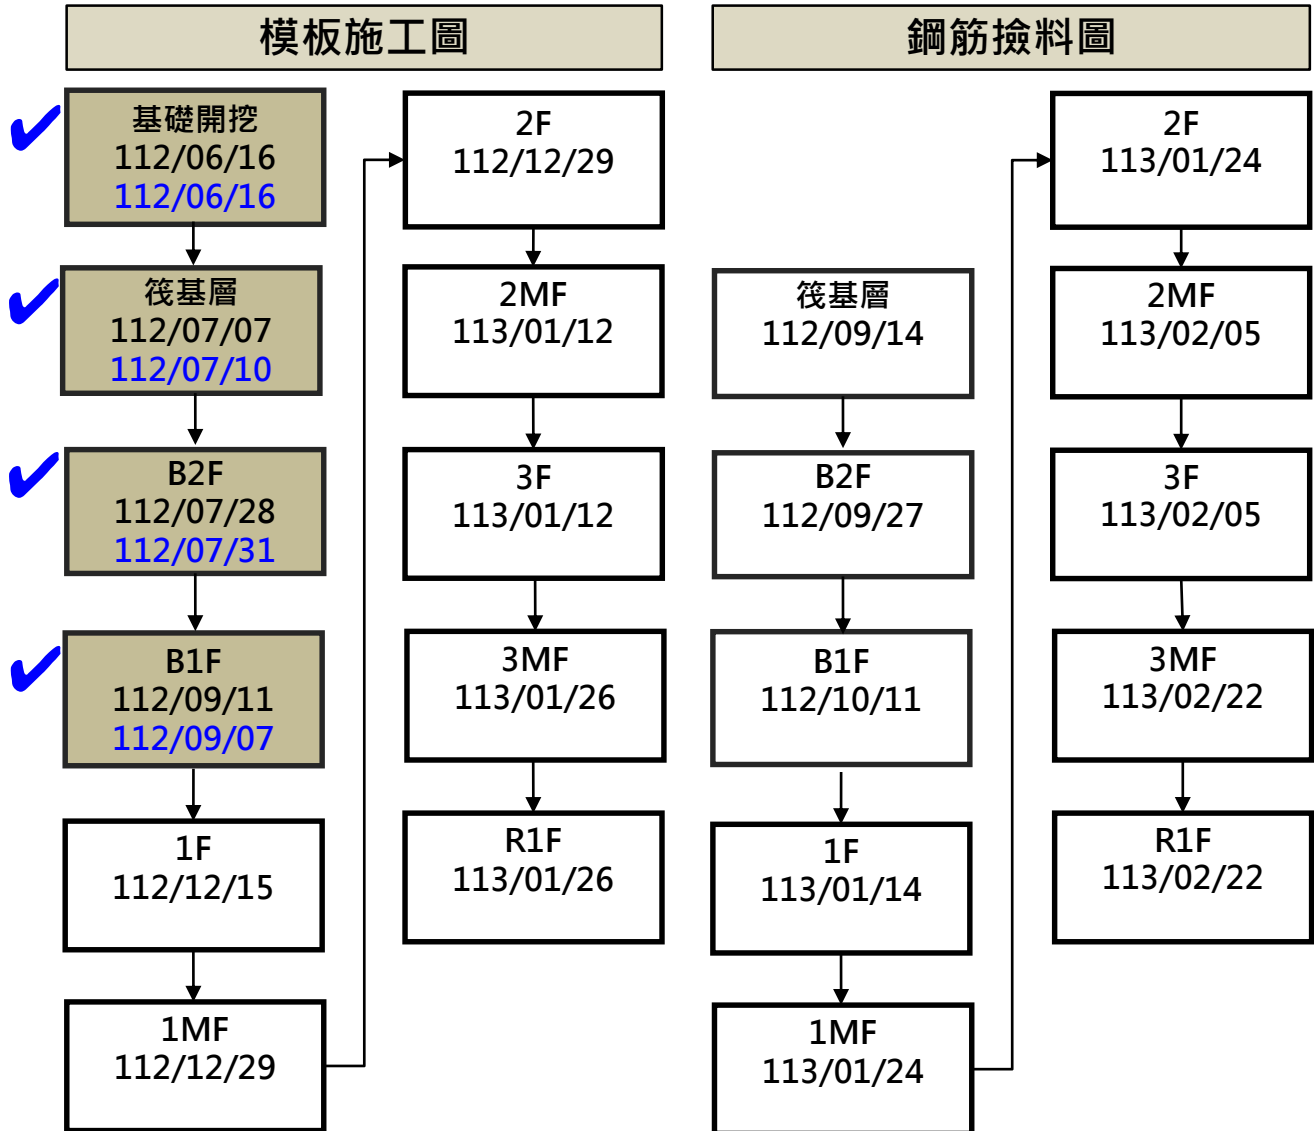

● 目標進度管控表 (C玄文)

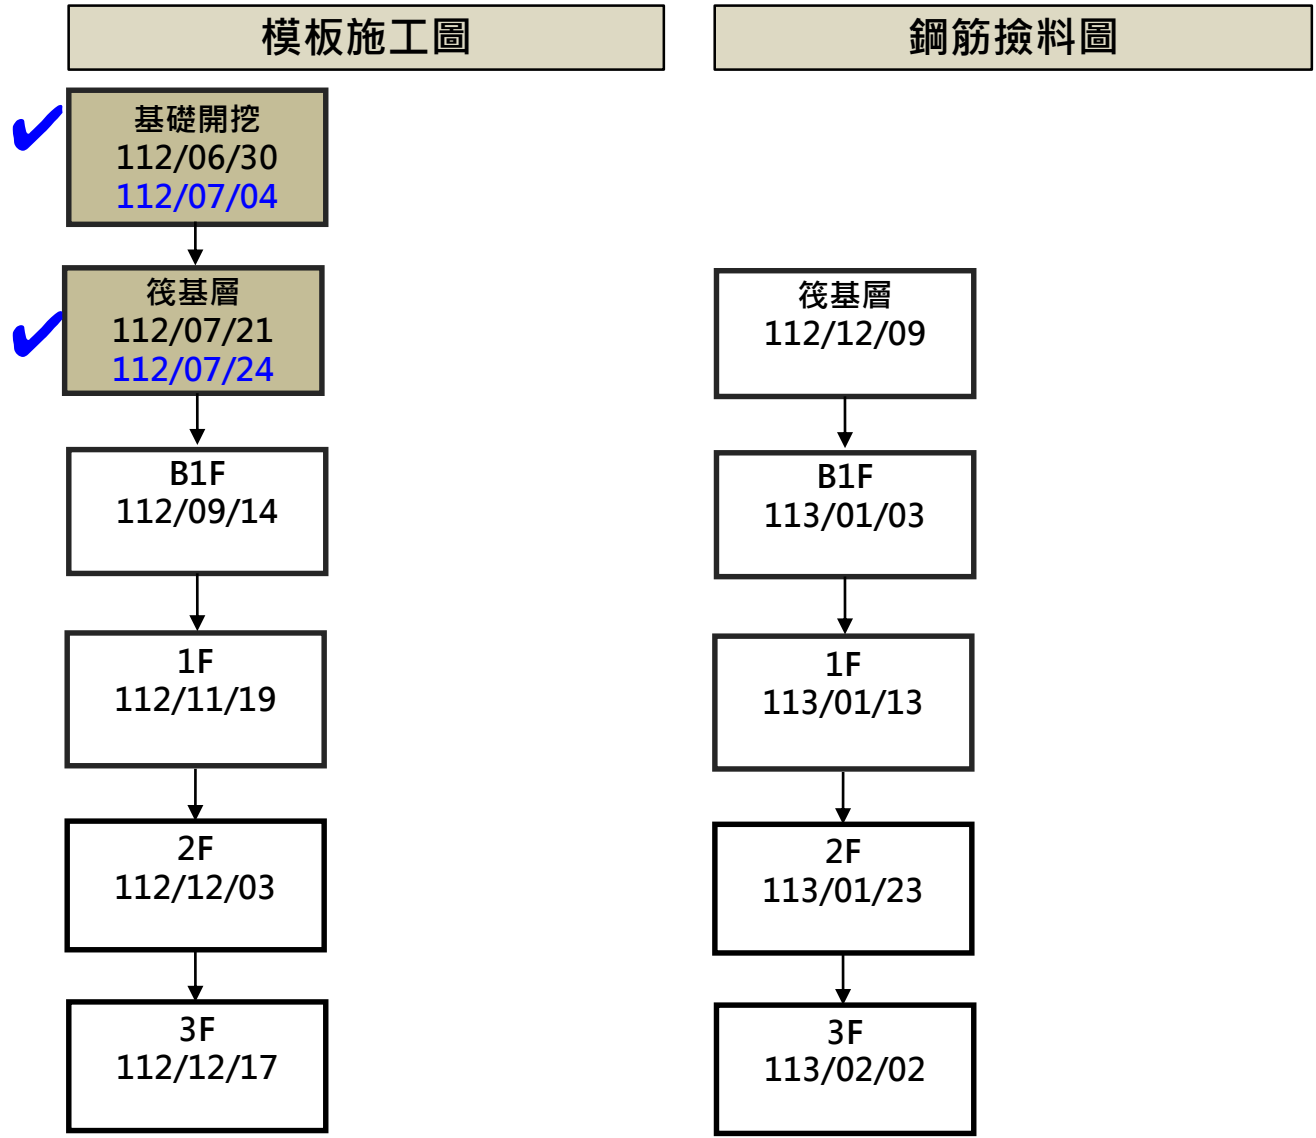

● 目標進度管控表 (B齋堂)

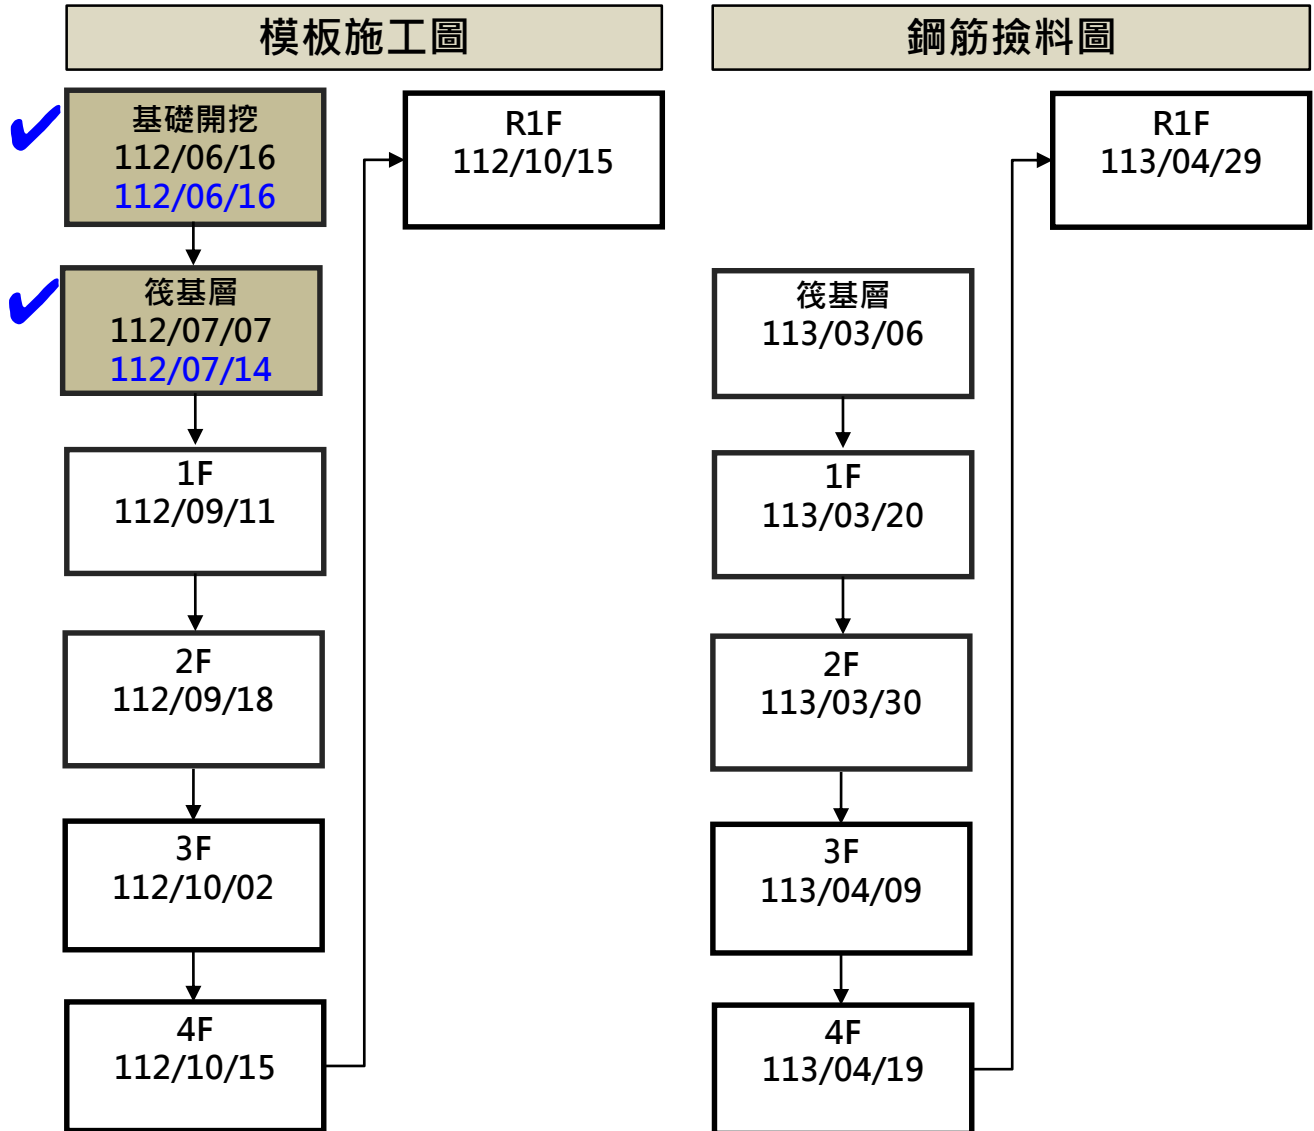


正覺寺玄奘文化宗教園區開發案

進度管理

- 排樁、基樁、於2023/09/04全部完成


	地工	預計開始	預計完成	實際完成
	主殿排樁	2023/01/05	2023/02/10	2023/02/04
	主殿基樁	2023/05/08	2023/07/13	2023/07/14
	女寮排樁	2023/02/11	2023/03/08	2023/03/08
	女寮基樁	2023/03/25	2023/05/09	2023/05/09
	玄文排樁	2023/03/06	2023/03/17	2023/03/23
	玄文基樁	2023/05/10	2023/05/24	2023/05/31
	齋堂排樁	2023/03/25	2023/04/14	2023/04/19
	齋堂基樁	2023/07/14	2023/09/14	2023/09/04
	司機排樁	2023/03/18	2023/03/24	2023/03/14

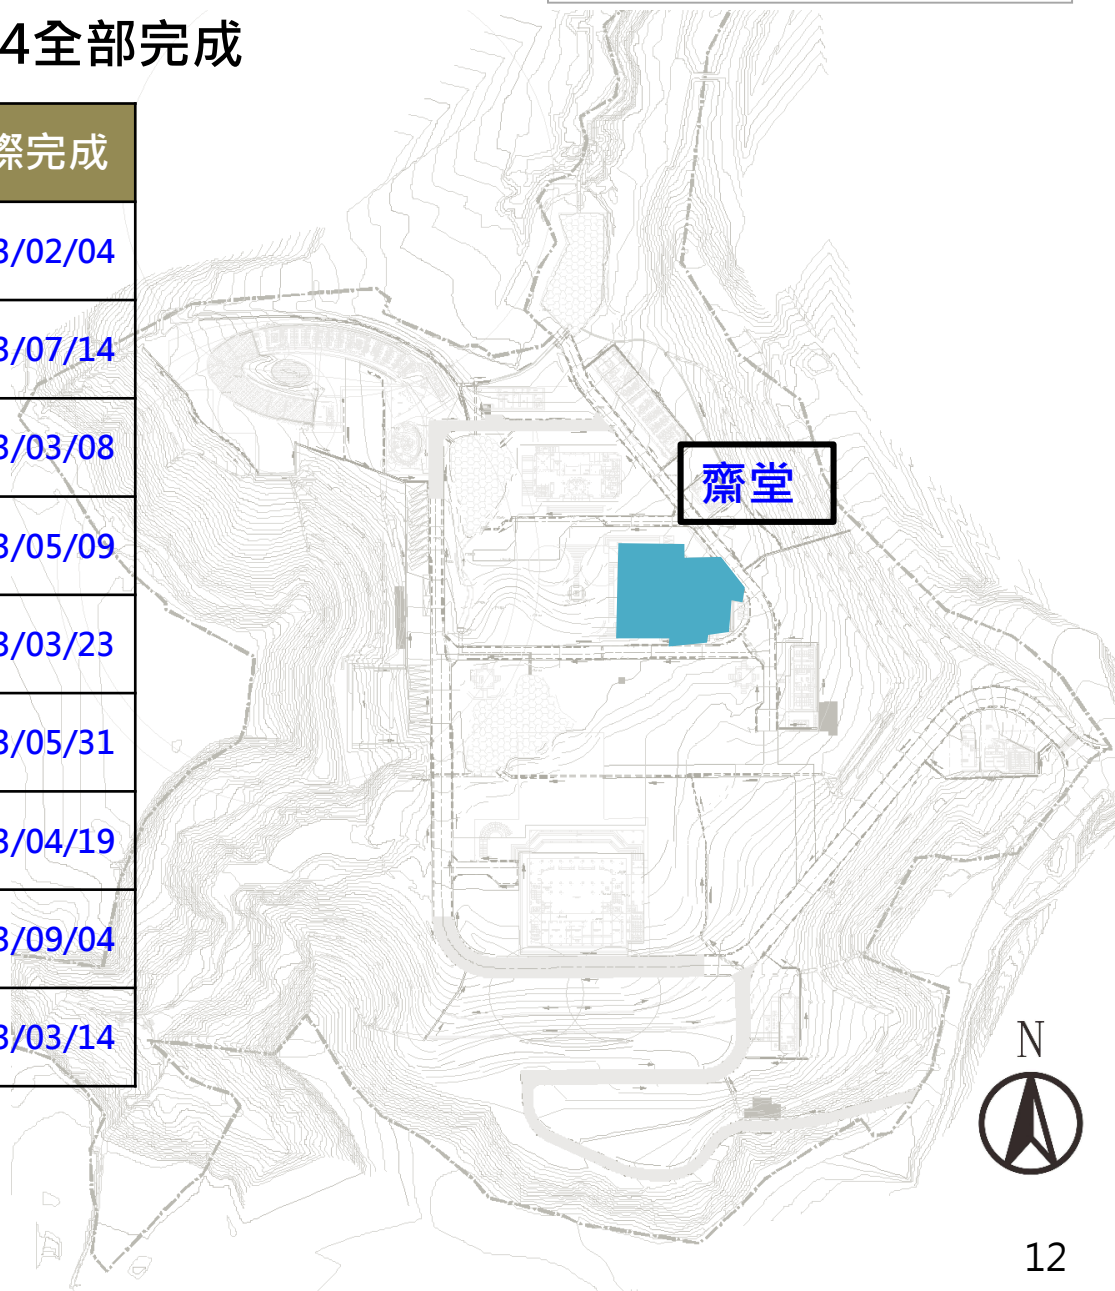

正覺寺玄奘文化宗教園區開發案

進度管理


● 齋堂全套管基樁總計67支(已全部完成)

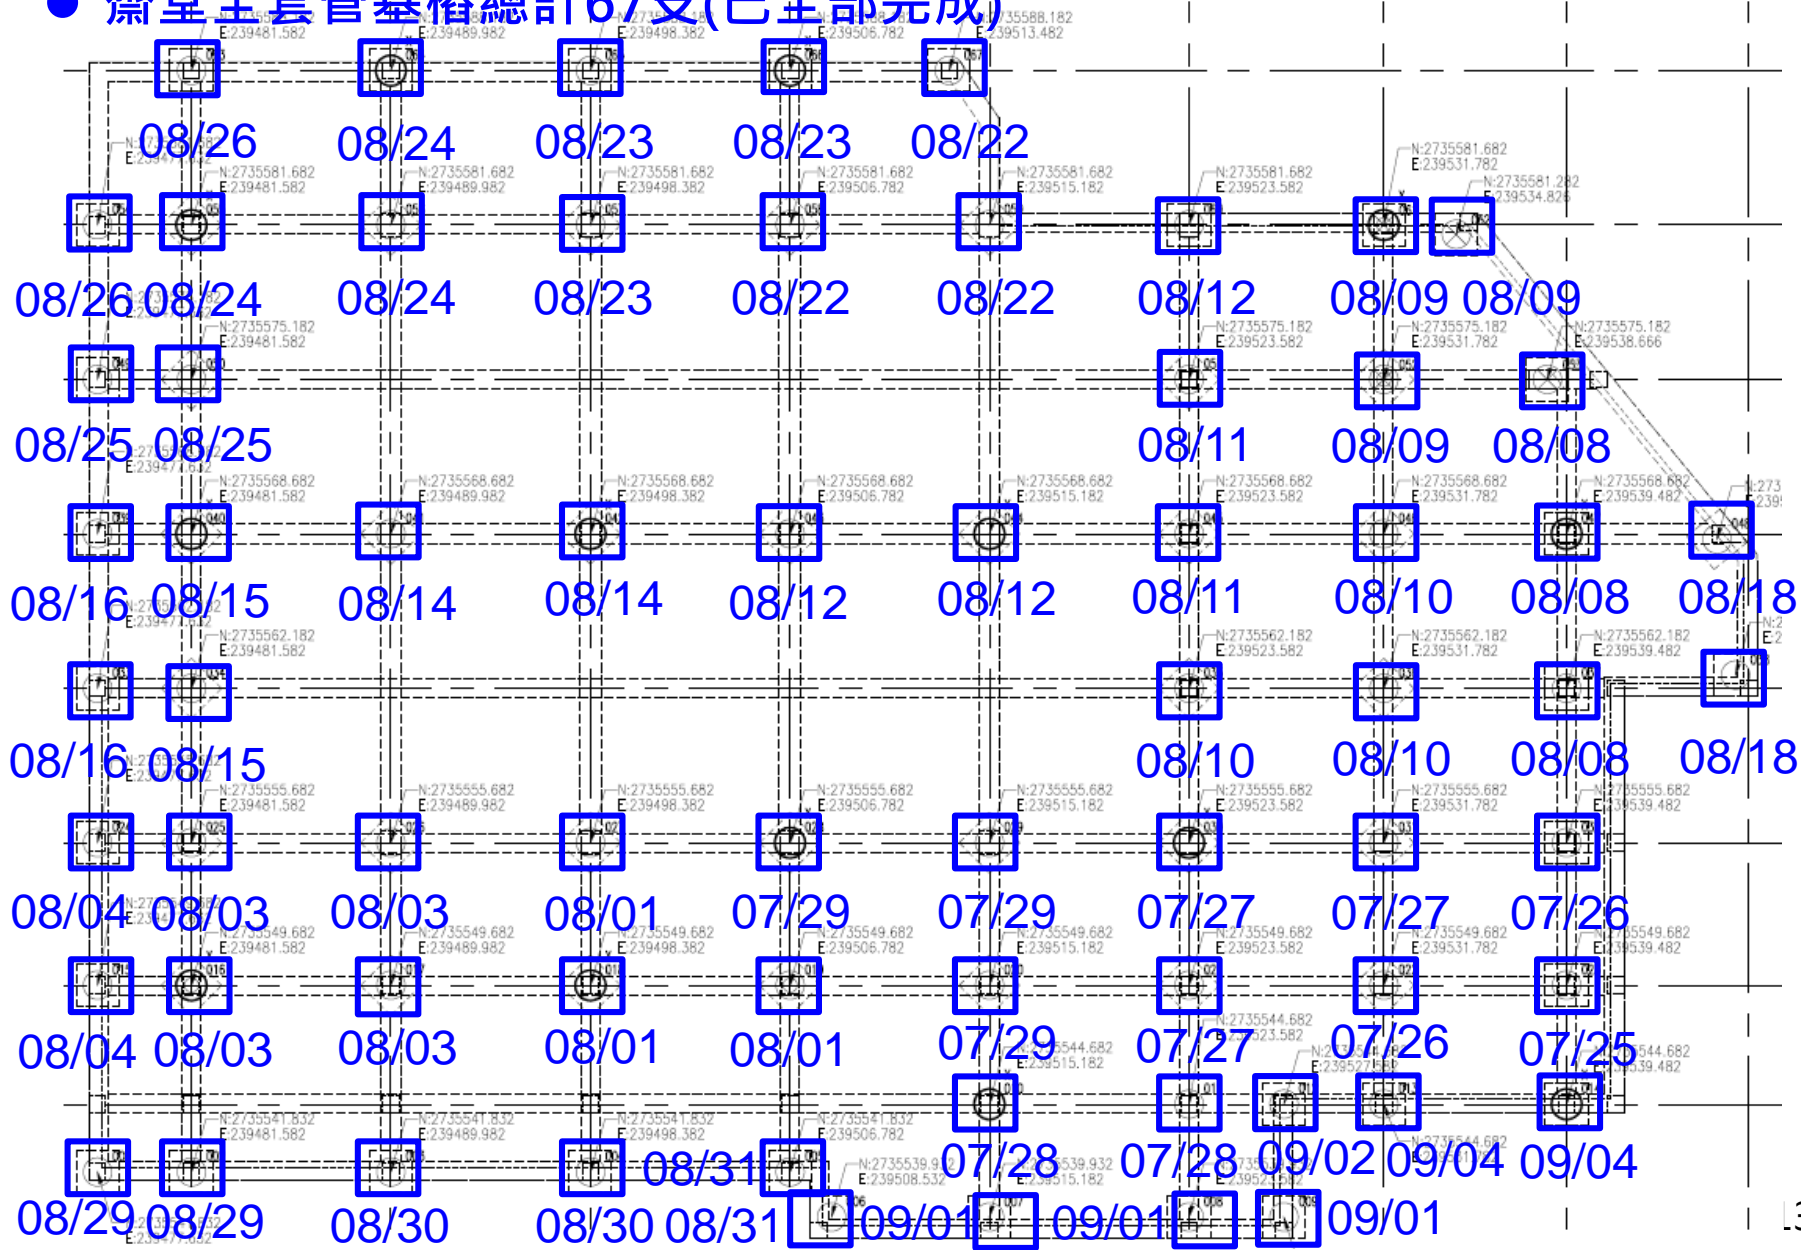



齋堂全套管基樁施作


齋堂全套管基樁判岩

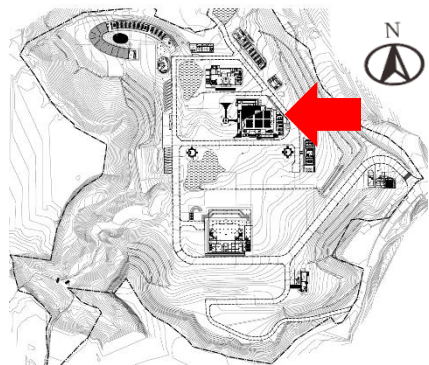



齋堂全套管基樁鋼筋籠查驗

齋堂全套管基樁深度查驗

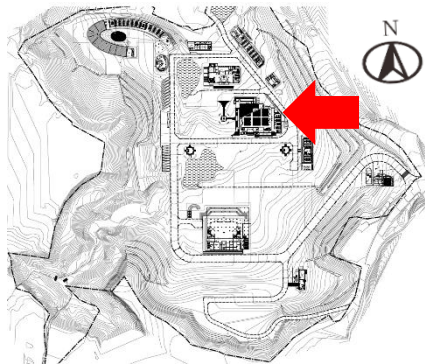




齋堂全套管基樁施作




齋堂全套管基樁判岩

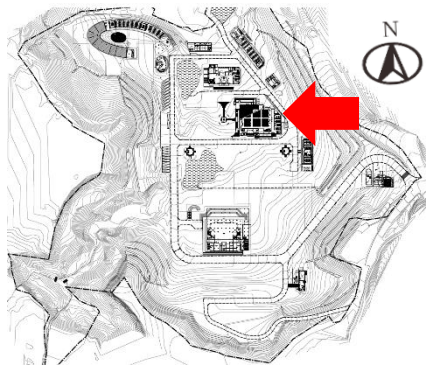




齋堂全套管基樁鋼筋籠查驗

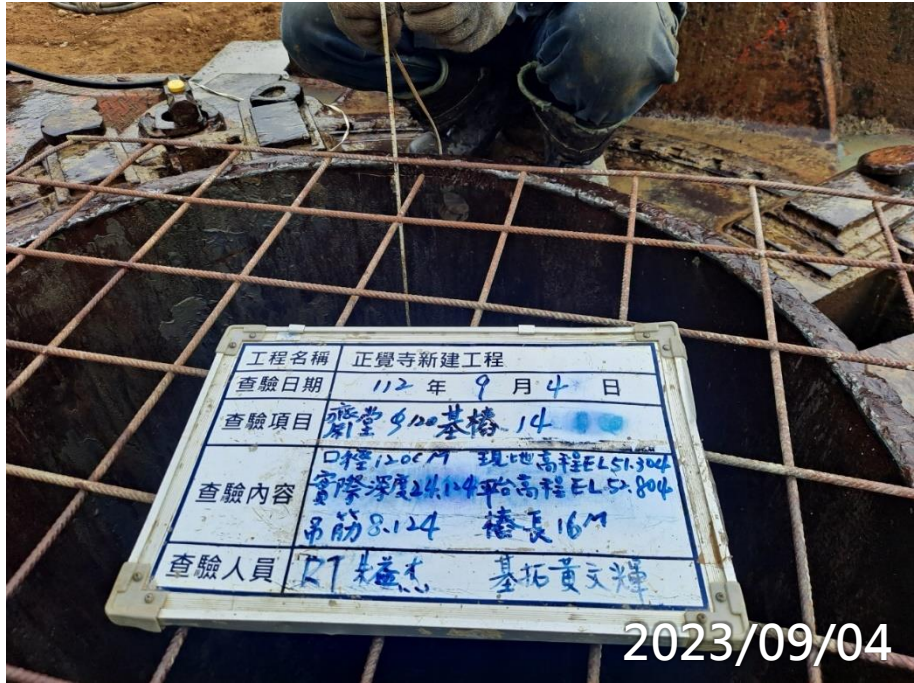

齋堂全套管基樁深度查驗

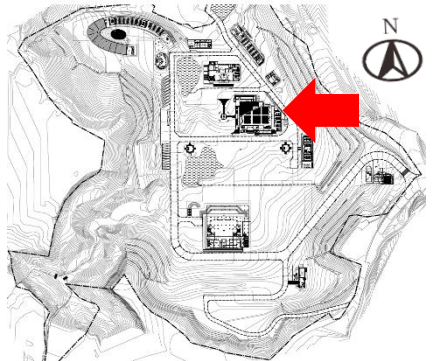




齋堂全套管基樁機具退場



齋堂全套管基樁機具退場

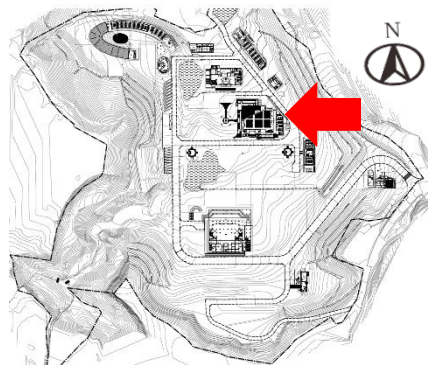




汙水廠、玄文動線鋼板鋪設




汙水廠、玄文動線鋼板鋪設

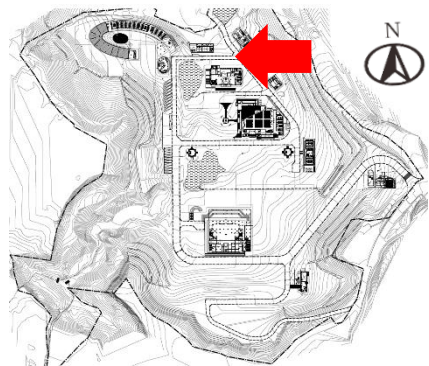



全區道路AC修繕

全區道路AC修繕

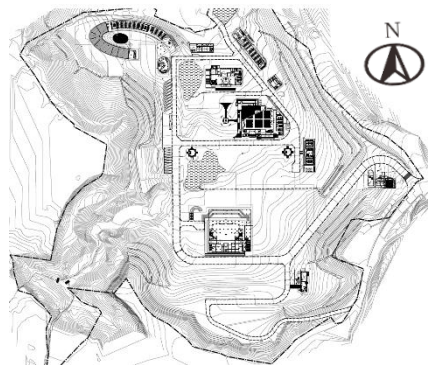




女寮施工便道管路埋設



女寮臨時水管配管

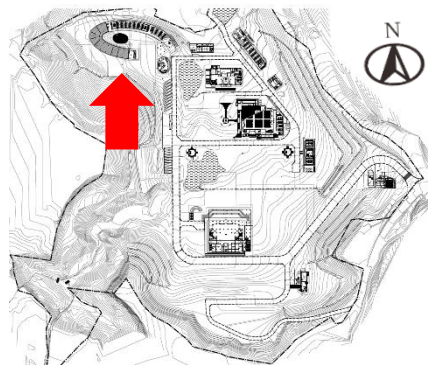




女寮臨時水管配管



污水處理廠臨時水電基礎座

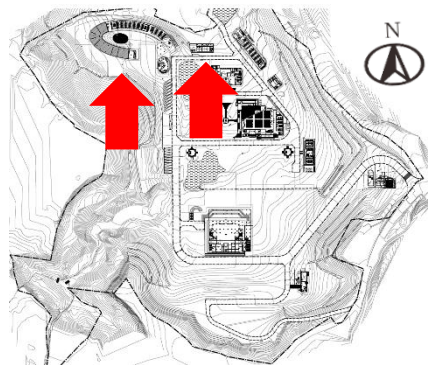

正覺寺玄奘文化宗教園區開發案

施工照片



臨時電電線材料進場查驗

臨時電電線材料進場查驗

