


正覺寺玄奘文化宗教園區開發案

進度管理

2024/02/21主殿土方工程開挖及女寮、污水工程進度

	工程進度	目標工期	實際完成
1-1	開工前行政程序		
1-1-1	申報開工	2022/07/15	2022/07/19
1-1-2	放樣勘驗	2022/07/26	2022/07/28
1-1-3	第一次變更設計	2023/07/21	2023/07/21
1-1-4	第二次變更設計	2023/11/24	2023/11/10
1-2	施工中作業		
1-2-1	土方開挖完成(汙水廠)	2023/10/23	2023/11/06
1-2-2	基礎版完成(汙水廠)	2023/11/16	2023/11/17
1-2-3	B1F版完成(汙水廠)	2024/01/22	2024/01/22
1-2-4	RF版完成(汙水廠)	2024/02/24	
1-2-5	2區土方開挖完成(女寮)	2023/11/09	2023/11/09
1-2-6	2區基礎版完成(女寮)	2023/12/02	2023/12/15
1-2-7	2區1F版完成(女寮)	2024/01/24	2024/01/29

正覺寺玄奘文化宗教園區開發案施工照片

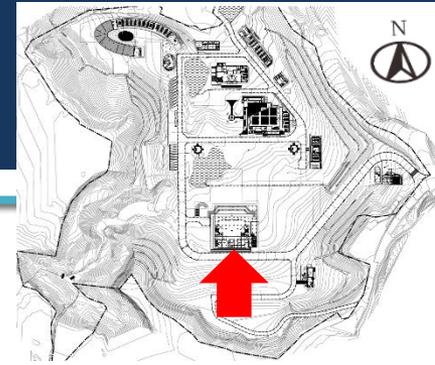

主殿土方開挖





主殿土方開挖



主殿土方開挖

主殿土方開挖

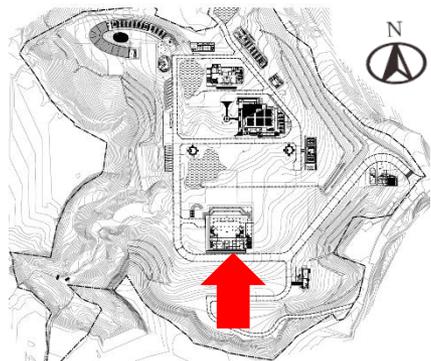


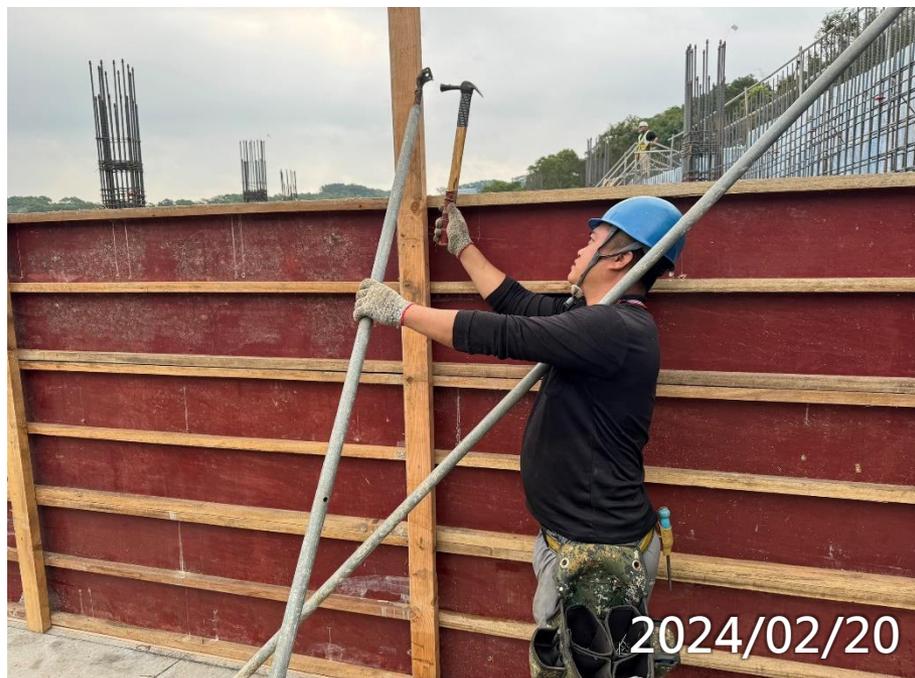

女寮2區1F柱牆模板組立



女寮2區1F柱牆模板組立

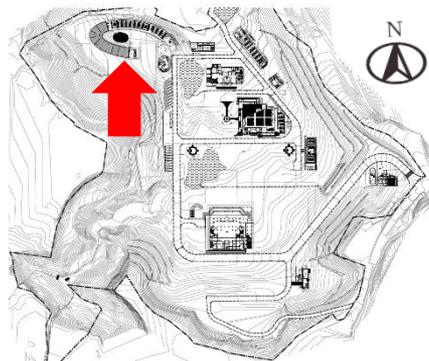




女寮2區1F柱牆鋼筋綁紮




女寮2區1F柱牆鋼筋綁紮

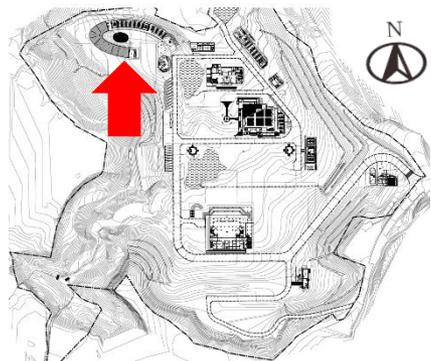




女寮1區基樁樁頭劣質打除

女寮1區基樁樁頭劣質打除

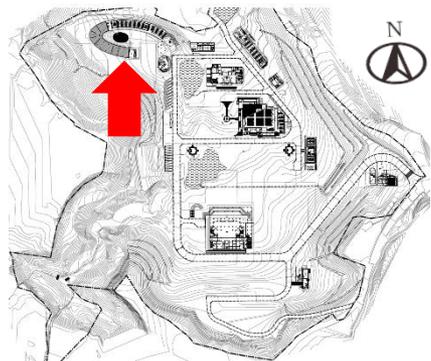




女寮1區噴漿護坡

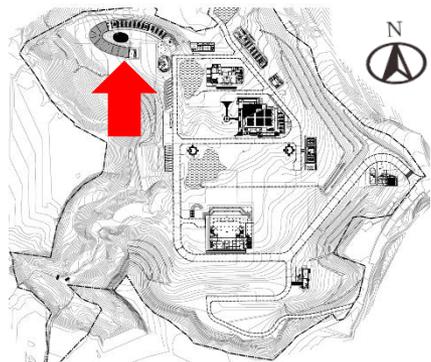


女寮1區噴漿護坡

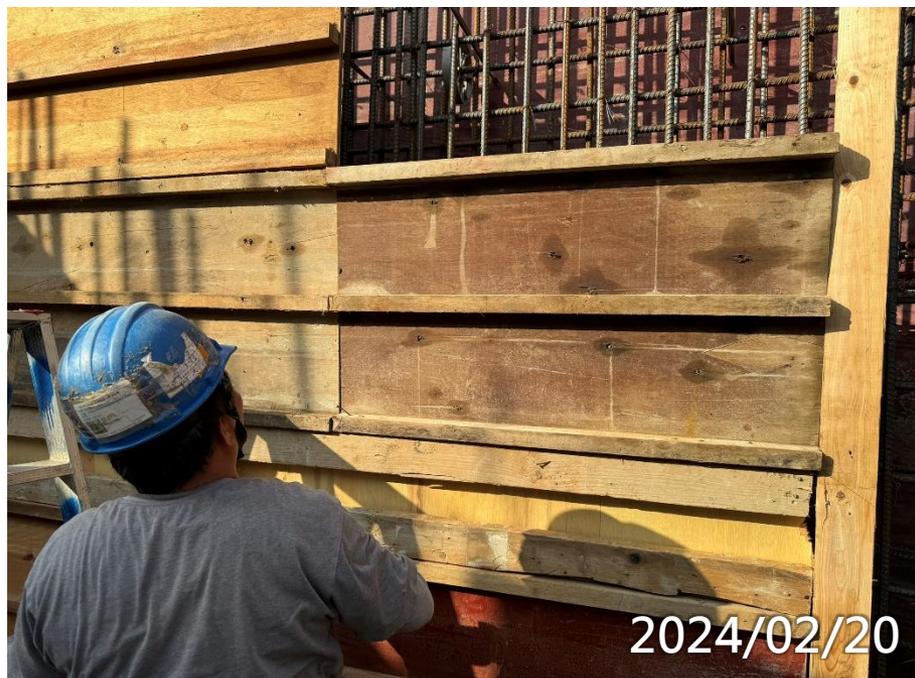


污水廠B1F牆柱模板組立



污水廠RF梁版模板組立

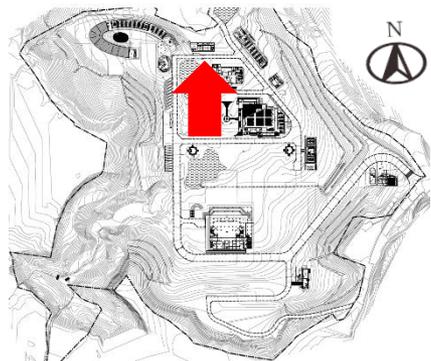

正覺寺玄奘文化宗教園區開發案施工照片

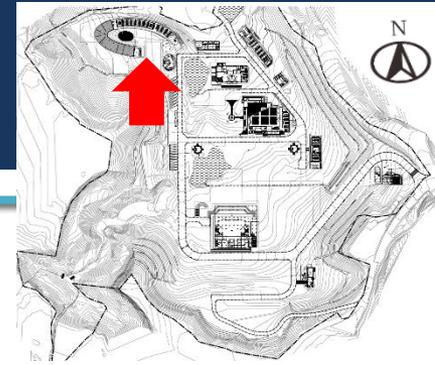


女寮1區噴漿護坡



女寮1區PC打底

正覺寺玄奘文化宗教園區開發案施工照片

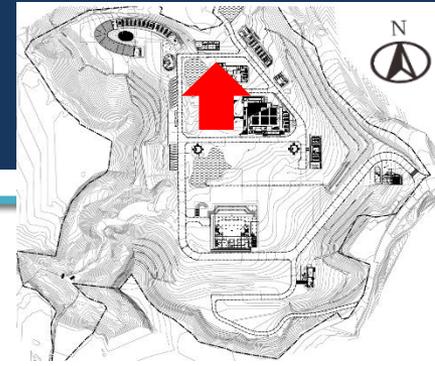


污水廠RF版梁鋼筋綁紮



污水廠RF版梁鋼筋綁紮

正覺寺玄奘文化宗教園區開發案施工照片

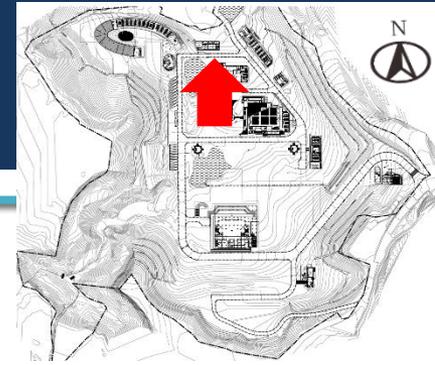


污水處理廠B1F柱牆模板組立



污水處理廠RF版梁模板組立

正覺寺玄奘文化宗教園區開發案施工照片

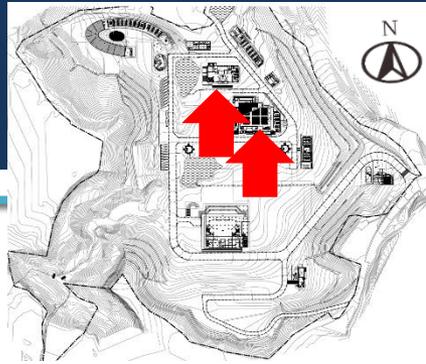


玄文地錨試錨



齋堂第一層地錨施作

正覺寺玄奘文化宗教園區開發案施工照片

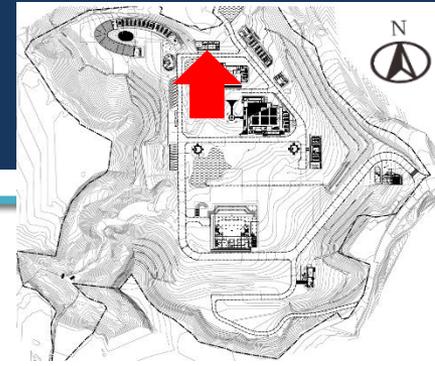


污水廠RF版水電配管



污水廠RF版水電配管查驗

正覺寺玄奘文化宗教園區開發案施工照片

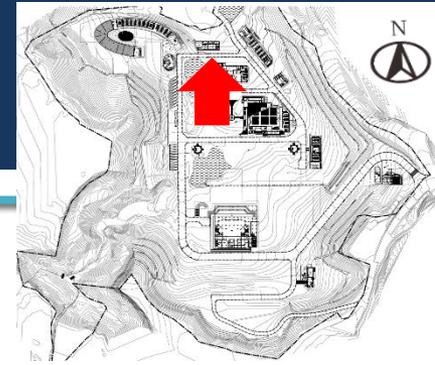

女寮2區1F水電配管



女寮2區1F水電配管
