


# 正覺寺玄奘文化宗教園區開發案

進度管理

## 2024/02/21主殿土方工程開挖及女寮、污水工程進度

	工程進度	目標工期	實際完成
1-1	<b>開工前行政程序</b>		
1-1-1	申報開工	2022/07/15	2022/07/19
1-1-2	放樣勘驗	2022/07/26	2022/07/28
1-1-3	第一次變更設計	2023/07/21	2023/07/21
1-1-4	第二次變更設計	2023/11/24	2023/11/10
1-2	<b>施工中作業</b>		
1-2-1	土方開挖完成(污水廠)	2023/10/23	2023/11/06
1-2-2	基礎版完成(污水廠)	2023/11/16	2023/11/17
1-2-3	B1F版完成(污水廠)	2024/01/22	2024/01/22
1-2-4	RF版完成(污水廠)	2024/02/24	
1-2-5	2區土方開挖完成(女寮)	2023/11/09	2023/11/09
1-2-6	2區基礎版完成(女寮)	2023/12/02	2023/12/15
1-2-7	2區1F版完成(女寮)	2024/01/24	2024/01/29

# 正覺寺玄奘文化宗教園區開發案施工照片

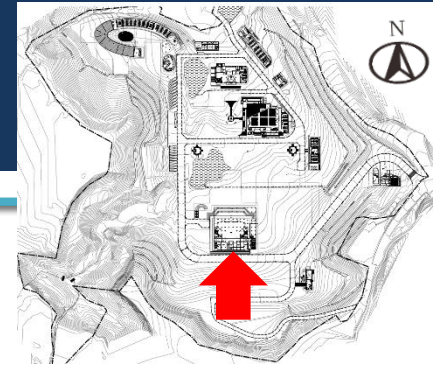

主殿土方開挖




主殿土方開挖






主殿土方開挖

主殿土方開挖

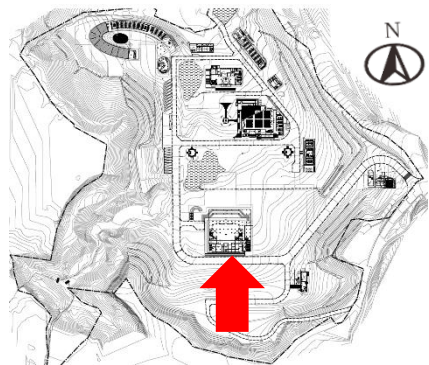




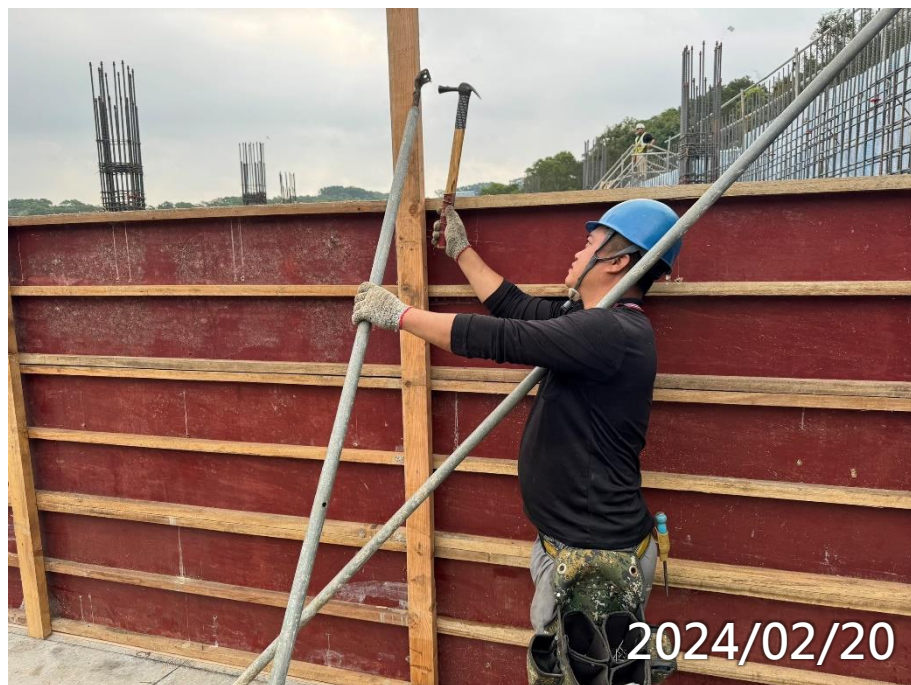

女寮2區1F柱牆模板組立



女寮2區1F柱牆模板組立

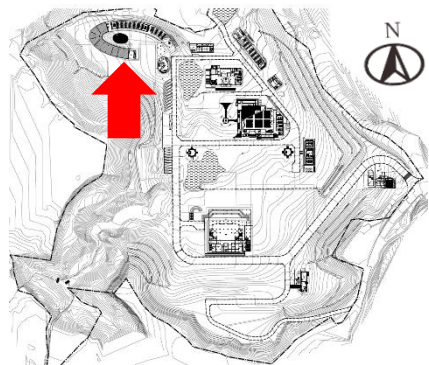






女寮2區1F柱牆鋼筋綁紮



女寮2區1F柱牆鋼筋綁紮

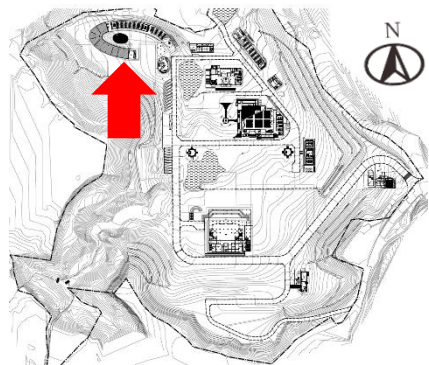






女寮1區基樁樁頭劣質打除


女寮1區基樁樁頭劣質打除

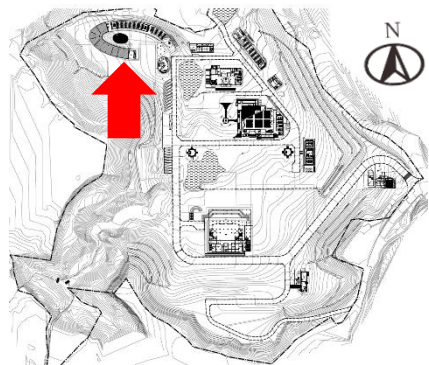





女寮1區噴漿護坡

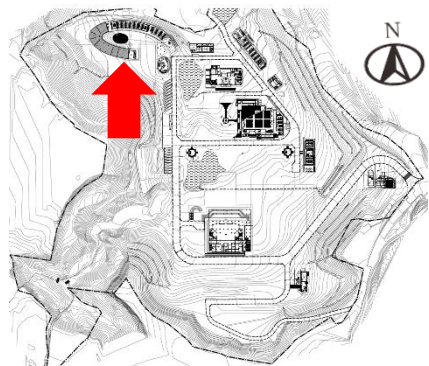

女寮1區噴漿護坡






污水廠B1F牆柱模板組立




污水廠RF梁版模板組立

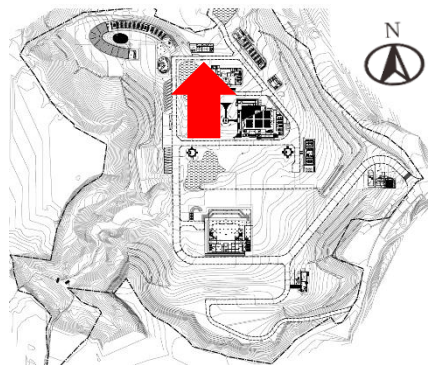



# 正覺寺玄奘文化宗教園區開發案施工照片

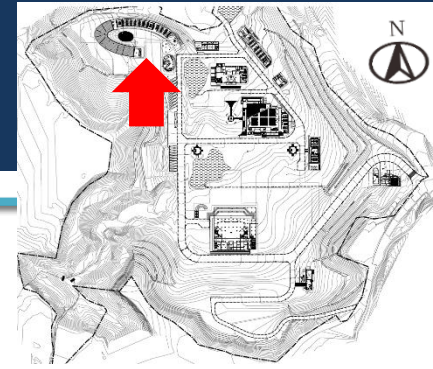


女寮1區噴漿護坡



女寮1區PC打底



# 正覺寺玄奘文化宗教園區開發案施工照片

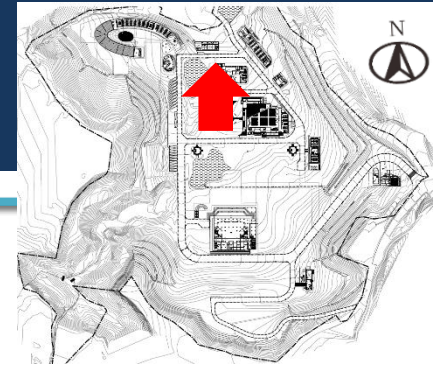


污水廠RF版梁鋼筋綁紮



污水廠RF版梁鋼筋綁紮



# 正覺寺玄奘文化宗教園區開發案施工照片

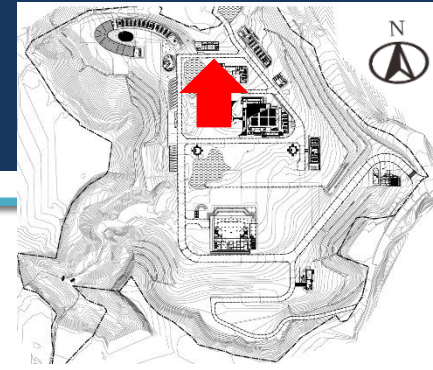


污水處理廠B1F柱牆模板組立



污水處理廠RF版梁模板組立



# 正覺寺玄奘文化宗教園區開發案施工照片

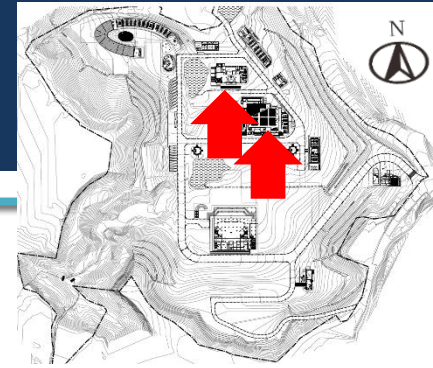


玄文地錨試錨



齋堂第一層地錨施作



# 正覺寺玄奘文化宗教園區開發案施工照片

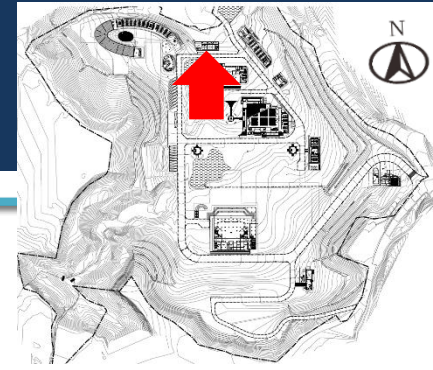


污水廠RF版水電配管



污水廠RF版水電配管查驗



# 正覺寺玄奘文化宗教園區開發案施工照片

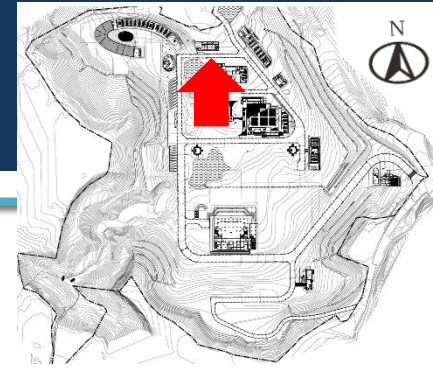

女寮2區1F水電配管



女寮2區1F水電配管
